

CP - ATELIER

Project Status Report — Management Review

As of 2026-06-01 · Live data from PostgREST · Homeland Group

PROJECT SNAPSHOT — CP-ATELIER TOWER

33

TOTAL TASKS
Across all areas

8

COMPLETED
24.2% done

25

PENDING
Scheduled ahead

0

OVERDUE
All tasks on schedule

Overall completion: 24.2% 8 of 33 tasks done

COMPLETION BY AREA

Basement Raft work 40% (6/15)

Column and Slab work 11% (2/18)

Area	Total Tasks	Completed	Remaining	% Done
Basement Raft work	15	6	9	40%
Column and Slab work	18	2	16	11%

POUR-WISE STATUS — BASEMENT RAFT WORK


Pour - 1 100%	Pour - 1 A 0%	Pour - 10 0%	Pour - 2 100%
Pour - 2 A 0%	Pour - 3 100%	Pour - 4 100%	Pour - 4 A 0%
Pour - 5 100%	Pour - 5 A 0%	Pour - 6 100%	Pour - 7 0%
Pour - 7 A 0%	Pour - 8 0%	Pour - 9 0%	

Green border = 100% complete · Teal = in progress · Gray = not started · Top strip = % filled

POUR-WISE STATUS — COLUMN AND SLAB WORK

Pour - 1 0%	Pour - 2 33%	Pour - 3 33%	Pour - 4 0%
Pour - 5 0%	Pour - 6 0%		

UPCOMING TASK DEADLINES (next 60 days from 2026-06-01)

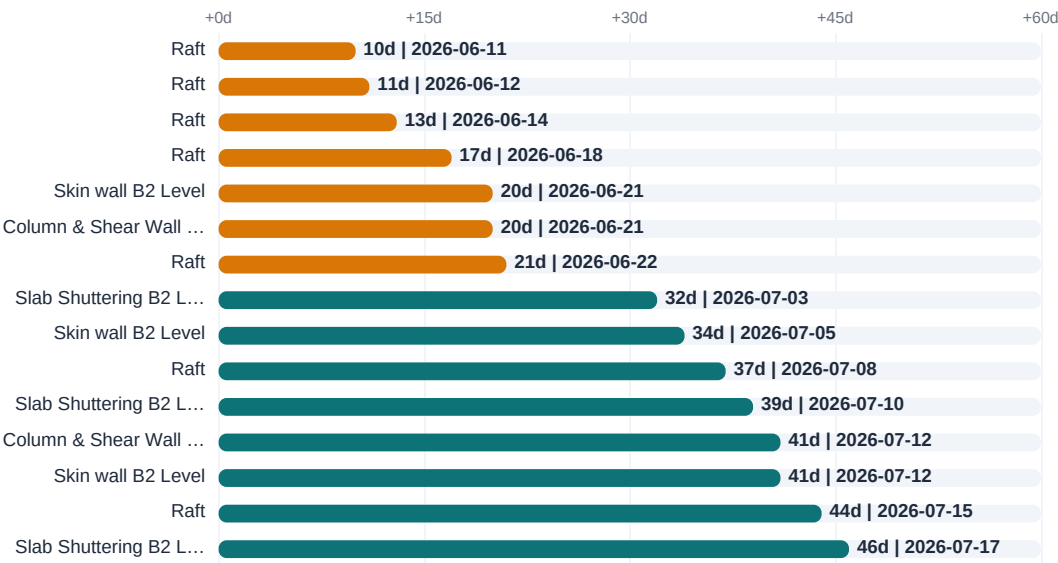

SCHEDULED TASK LIST — ALL PENDING

Task Name	Area	Sub-Area	Due Date	Days Left
Raft	Basement Raft work	Pour - 2 A	2026-06-11	10d
Raft	Basement Raft work	Pour - 7	2026-06-12	11d
Raft	Basement Raft work	Pour - 4 A	2026-06-14	13d
Raft	Basement Raft work	Pour - 5 A	2026-06-18	17d
Skin wall B2 Level	Column and Slab work	Pour - 1	2026-06-21	20d
Column & Shear Wall Reinforcement At B2 Level	Column and Slab work	Pour - 1	2026-06-21	20d
Raft	Basement Raft work	Pour - 7 A	2026-06-22	21d
Slab Shuttering B2 Level	Column and Slab work	Pour - 1	2026-07-03	32d
Skin wall B2 Level	Column and Slab work	Pour - 3	2026-07-05	34d
Raft	Basement Raft work	Pour - 8	2026-07-08	37d
Slab Shuttering B2 Level	Column and Slab work	Pour - 2	2026-07-10	39d
Column & Shear Wall Reinforcement At B2 Level	Column and Slab work	Pour - 4	2026-07-12	41d
Skin wall B2 Level	Column and Slab work	Pour - 4	2026-07-12	41d
Raft	Basement Raft work	Pour - 10	2026-07-15	44d
Slab Shuttering B2 Level	Column and Slab work	Pour - 3	2026-07-17	46d
Raft	Basement Raft work	Pour - 9	2026-07-17	46d
Column & Shear Wall Reinforcement At B2 Level	Column and Slab work	Pour - 5	2026-07-19	48d
Skin wall B2 Level	Column and Slab work	Pour - 5	2026-07-19	48d
Raft	Basement Raft work	Pour - 1 A	2026-07-20	49d
Slab Shuttering B2 Level	Column and Slab work	Pour - 4	2026-07-24	53d

Task Name	Area	Sub-Area	Due Date	Days Left
Skin wall B2 Level	Column and Slab work	Pour - 6	2026-07-26	55d
Column & Shear Wall Reinforcment At B2 L...	Column and Slab work	Pour - 6	2026-07-26	55d
Skin wall B2 Level	Column and Slab work	Pour - 2	2026-07-28	57d
Slab Shuttering B2 Level	Column and Slab work	Pour - 5	2026-07-31	60d
Slab Shuttering B2 Level	Column and Slab work	Pour - 6	2026-08-07	67d

KEY OBSERVATIONS & OUTLOOK

01

Zero Overdue Tasks — Project On Schedule

All 25 pending tasks have future due dates. CP-Atelier is currently tracking well against its planned schedule with no slippages recorded.

02

Basement Raft Work — 40% Complete (6/15 pours done)

Pour-1 through Pour-6 are complete. Pours 7, 7A, 8, 9, 10 and variants 1A, 2A, 4A, 5A remain. Next raft pours are due from 11-Jun through 15-Jul.

03

Column & Slab Work — 11% Complete (2/18 tasks done)

This area requires accelerated focus. Only Pour-2 and Pour-3 have partial completions. Key milestones — Skin Wall and Column Reinforcement — are due by 21-Jun (7 tasks within 21 days).

04

No Immediate Deadline Pressure (next 7 days)

No tasks are due within 7 days. 7 task(s) are due within the next 21 days and should be kept on radar.

Report auto-generated from live PostgREST data · Homeland Group · 2026-06-01 · CP-Atelier tower within Homeland Global Park project.
