

HOMELAND GLOBAL PARK

Project Status & Overdue Task Report

Prepared for Management Review | As of 2026-06-01 | Homeland Group

PROJECT SNAPSHOT

264

TOTAL TASKS
All towers & areas

111

COMPLETED
42.0% done

110

PENDING
In progress

43

OVERDUE
Past due date

Overall completion: 42.0%

111 of 264 tasks done


OVERDUE TASK ANALYSIS — Days Past Due to Tomorrow (2026-06-02)

Overdue by Delay Bucket



Days counted from due date to 2026-06-02. Today's tasks are still pending.

Overdue by Work Area



OVERDUE TASK DETAIL (43 tasks)


Task Name	Area	Sub-Area	Due Date	Days Past
Panel No -3	D -Wall Work	Type - B	2026-05-23	10d
Panel No -2	D -Wall Work	Type - B	2026-05-24	9d
B10	HGP - Sales Office	Footing	2026-05-25	8d
Panel No. 18	D -Wall Work	Type - D	2026-05-25	8d
Panel No -1	D -Wall Work	Type - D	2026-05-25	8d
B11	HGP - Sales Office	Footing	2026-05-26	7d
(B-D/2-8)	HGP - Sales Office	Plinth Beam	2026-05-26	7d
Panel No -20	D -Wall Work	Type - B	2026-05-26	7d
B12	HGP - Sales Office	Footing	2026-05-27	6d
Panel No -21	D -Wall Work	Type - B	2026-05-27	6d

Task Name	Area	Sub-Area	Due Date	Days Past
Panel No -24	D -Wall Work	Type - B	2026-05-27	6d
D8	HGP - Sales Office	Pedestal	2026-05-28	5d
C8	HGP - Sales Office	Pedestal	2026-05-28	5d
D7	HGP - Sales Office	Pedestal	2026-05-28	5d
C7	HGP - Sales Office	Pedestal	2026-05-28	5d
A10	HGP - Sales Office	Footing	2026-05-28	5d
(A-D/8-12)	HGP - Sales Office	Plinth Beam	2026-05-28	5d
Panel No. 19	D -Wall Work	Type - D	2026-05-28	5d
Panel No -22	D -Wall Work	Type - B	2026-05-28	5d
Panel No -1	D -Wall Work	Type - B	2026-05-28	5d
A-11	HGP - Sales Office	Pedestal	2026-05-29	4d
A-12	HGP - Sales Office	Pedestal	2026-05-29	4d
A-10	HGP - Sales Office	Pedestal	2026-05-29	4d
A-9	HGP - Sales Office	Pedestal	2026-05-29	4d
A11	HGP - Sales Office	Footing	2026-05-29	4d
L - Shape Panel	D -Wall Work	Type - B	2026-05-29	4d
Panel No -23	D -Wall Work	Type - B	2026-05-29	4d
D-10	HGP - Sales Office	Pedestal	2026-05-30	3d
D-12	HGP - Sales Office	Pedestal	2026-05-30	3d
C-9	HGP - Sales Office	Pedestal	2026-05-30	3d
B-11	HGP - Sales Office	Pedestal	2026-05-30	3d
B-12	HGP - Sales Office	Pedestal	2026-05-30	3d
C-10	HGP - Sales Office	Pedestal	2026-05-30	3d
D-9	HGP - Sales Office	Pedestal	2026-05-30	3d
D-11	HGP - Sales Office	Pedestal	2026-05-30	3d
C-12	HGP - Sales Office	Pedestal	2026-05-30	3d
C-11	HGP - Sales Office	Pedestal	2026-05-30	3d
B-10	HGP - Sales Office	Pedestal	2026-05-30	3d
B-9	HGP - Sales Office	Pedestal	2026-05-30	3d
A12	HGP - Sales Office	Footing	2026-05-30	3d
Structure Fabrication & Supply	HGP - Sales Office	Interior / Design Wo...	2026-05-30	3d
Total - 322	PCC	Pour - 2	2026-05-30	3d
Total - 322	PCC	Pour - 1	2026-05-30	3d

AREA-WISE OVERDUE SUMMARY

Work Area	Overdue	% of Overdue	Max Days Past	Avg Days Past
HGP - Sales Office	29	67.4%	8d	4.1d
D -Wall Work	12	27.9%	10d	6.4d
PCC	2	4.7%	3d	3.0d

DAYS-PAST-DUE DISTRIBUTION (task count per day of delay)

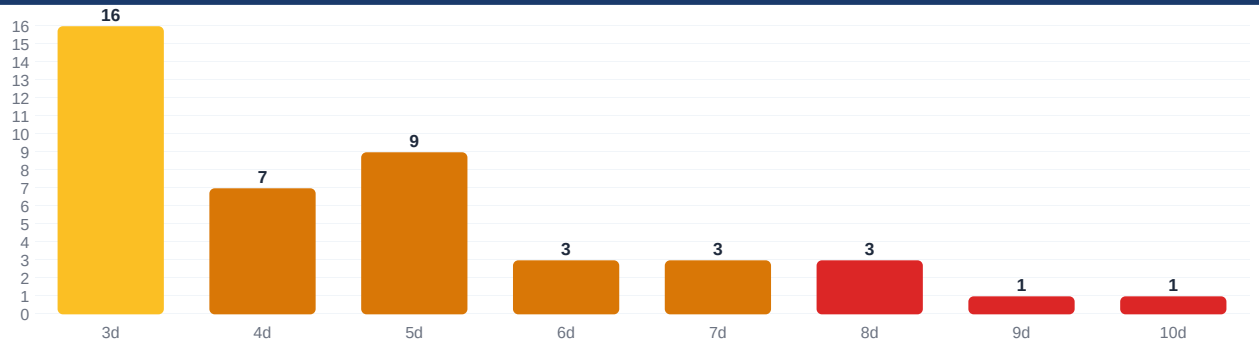

X-axis: days overdue (measured to tomorrow 2026-06-02). Red = 8+ days, Amber = 4-7 days, Yellow = 1-3 days.

KEY OBSERVATIONS & RECOMMENDED ACTIONS

01	HGP Sales Office — 29 overdue tasks (67% of all overdue) This area has the highest concentration of overdue tasks. Immediate re-prioritisation and resource deployment is recommended to prevent further schedule slippage.
02	D-Wall Work — 12 overdue tasks (28%) Diaphragm Wall panel work is behind schedule. Panel Nos. 1–3 are most critical at 8–10 days overdue. Review structural sequencing and labour availability.
03	PCC Work — 2 overdue tasks (5%) Minor overdue items in PCC area. Low overall risk but should be closed out promptly to avoid cascading impact on downstream activities.
04	Overall Completion at 42.0% (111/264 tasks done) 110 tasks are currently on track (pending/in-progress). Addressing the 43 overdue tasks will push overall completion comfortably above 50%.

Report auto-generated from live PostgREST data · Homeland Group · 2026-06-01 · Days past due calculated to tomorrow (2026-06-02) per management requirement.
